



Sanitary Contract 955 (Powder Mill Interceptor Improvements & Stream Restoration)

June 02, 2020

PROJECT LIMITS

Sanitary Contract 955 comprises of three distinct phases of work. Phases I and II are located within the limits of Powder Mill Park with Northern Parkway to the west and Parkview Ave to the east and Elderon Ave to the north and Liberty Rd (MD-26) to the south. See Figure 1.

Phase I involves building a new interceptor sewer and Phase II involves Stream Restoration of the Powder Mill Branch. Activities for Phase I and II will occur in parallel.

Phase III is located in Leakin Park, with Windsor Mill Rd to the north and Franklinton Rd to the south. The objective of SC955 Phase III is to build a permanent access road for the sanitary sewer assets (pipes and manholes) that were rehabilitated under another project (SC977). See Figure 2.



Figure 1: SC955 Phase I & II – Powder Mill Park

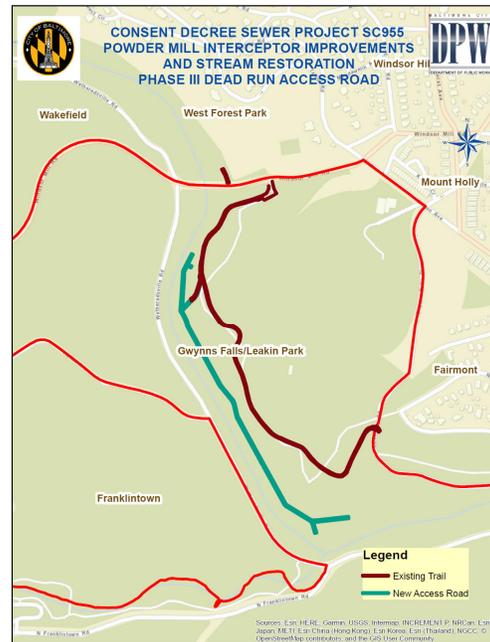


Figure 2: SC955 Phase III – Leakin Park

Project SC955 was given the official notice to proceed effective June 1, 2020. The project duration is approximately 18 months, resulting in a finish date of late November 2021.

Work in Progress

- This being at the very start of the project, all work on site is very preliminary. The contractor will perform site surveys, take tree inventory and establish erosion and sediment controls.

Upcoming Activity as of week of 06/08/2020

- During the first two weeks of the project (June 1 – June 12) the contractor (Metra Industries) will establish limit of disturbance (LOD) stakes based on a site survey. The LOD defines the area within which all land disturbing construction activity is allowed to take place.
- During the last two weeks of June, the contractor will commence vegetation clearing activities within Powder Mill Park and Leakin Park.
- Presence of Heavy Construction vehicles, equipment and construction noise is expected during the construction. The construction hours for this project is between 7:00 AM – 5:00 PM,

We hope this provides insights for upcoming work as we strive to timely and safely complete this project. If you have any questions, you may call Indranil (Neil) Goswami at (410) 396-4700, Monday through Friday, between 8:30 AM and 4:30 PM. Additional information and resources are also available on our website <https://publicworks.baltimorecity.gov/>

Sincerely,



Angela Cornish
Construction Project Supervisor II
DPW, Office of Engineering & Construction
angela.cornish@baltimorecity.gov
