

# DEPARTMENT OF PUBLIC WORKS

## Sanitary Sewer Modified Consent Decree

### Project Facts



## SC #1021:

### CCTV Inspection of Sanitary Sewers in in Baltimore City - Zone C

#### Project Purpose

To comply with the conditions of the City's Modified Consent Decree with the U.S. EPA and MDE

- To inspect a sewer system that is up to 100 years old
- To prioritize pipe rehabilitation work through condition assessment
- To indirectly:
  - improve sewage flows and pipe capacity
  - To reduce/eliminate sewer overflows
  - To eliminate street closures due to sewer pipe collapses
  - To improve water quality in streams
  - To prevent sewer back-ups into private property


#### Project Area Map



#### Project History

In 2002 the City of Baltimore (City) entered a Consent Decree with the U.S. Environmental Protection Agency (EPA) and the Maryland Department of the Environment (MDE). A Consent Decree is an agreement made in court by the parties to settle a suit in equity. In 2017, the Modified Consent Decree (MCD) was entered to address sewer system deficiencies in a proactive program by 2030. More information on the Consent Decree can be found at: <http://publicworks.baltimorecity.gov/>

#### Project Schedule

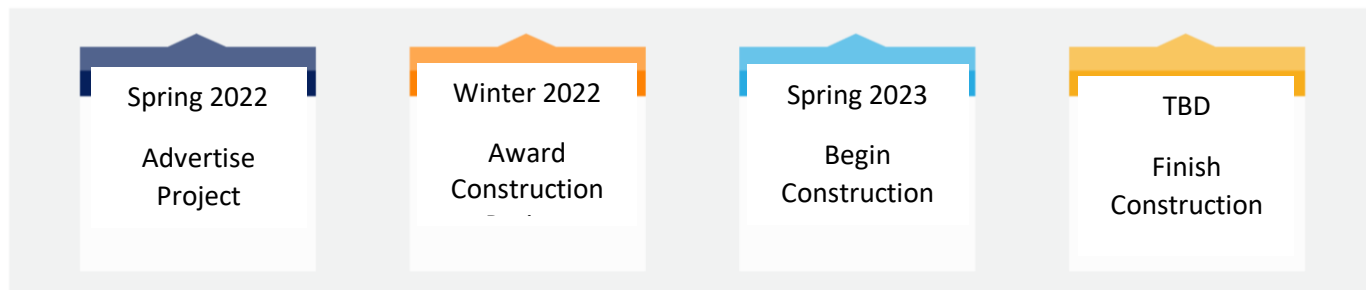

# DEPARTMENT OF PUBLIC WORKS

## Sanitary Sewer Modified Consent Decree

### Project Facts



## SC #1021:

### CCTV Inspection of Sanitary Sewers in Baltimore City

#### Project Updates

- NTP 03-27-2023
- Authorized Time 1,097 CCD
- Authorized Total 1,695,300.00
- Days Used to Date 361 CCD (32.9%)
- Days Remaining 736 CCD
- Work Completed \$95,499.06 (5.63%)
- Contract Completion Date 03-27-2026
- MBE Goals 54.5%      MBE to Date: \$44,971.88 (48.50%)
- WBE Goal 5%      WBE to Date: \$41,368.29 (44.61%)
- Currently No crews onsite currently (recently crews were out locating CNL manholes)
- WO #001,002 CCTV is currently being reviewed.
- WO # 003 CCTV package has been submitted and is under review as of 2/29/24.
- WO #001, and 002 manhole submittals have been sent back as revised and resubmitted 11/15/23. Packages were submitted on 3/5/2024 and are currently under review.
- WO # 003 Manhole submittals were submitted on 3/5/2024 and are currently under review.
- Currently there has not been any active work on the project since early March 2024. WO# 004 (CCTV only) is currently being packaged to be sent out to the contractor but will be pending until some of the recent work order packages are approved. Contractor sent a crew out to complete CCTV segments from previous work orders on 3/4/2024.

#### Project Activities

- CCTV of Sanitary Sewers (20,100 LF)
- Cleaning of Sanitary Sewers (20,100 LF)
- Replacement of Sanitary Sewers (12,100 LF)
- Installation of new Sanitary Sewers (8,000 LF)
- Reconnection of Sanitary Sewer (200 EA)
- Vertical Replacement of Manholes (690 V. LF)
- Vertical Manhole Installation (750 V. LF)
- Inspection of Manholes
- Cleaning of Manholes
- Removal of Excessive Grease & Roots
- Restoration of pavement, alleys, and sidewalks, and site
- Associated wastewater by-pass pumping or control of flows of sewers and/or manholes



If you have any project-related questions, please call (410) 396-4700, Monday through Friday, between 8:30 AM and 4:30 PM. Additional information and resources are also available on our website <https://publicworks.baltimorecity.gov/>

