



**Sanitary Contract 910 (Improvements to the Sanitary Sewer Collection System  
in the Herring Run Sewershed, Part 2: Chinquapin Run)**

August 01, 2021

To whom it may concern,

Sanitary Contract 910 is underway, and work is being completed at multiple locations. Work activities primarily consist of replacement and upsizing of sanitary sewers by open-cut excavation, cured-in-place pipe lining (CIPP), construction of new manholes, and stream stabilization along Chinquapin Run.

The purpose of this project is to:

- Repair the aging sewer system
- Prevent sewer back-ups into private property
- Reduce/eliminate sewer overflows
- Improve sewage flows and pipe capacity
- Improve stream water quality
- Maintain and enhance existing bedrock and bed features
- Stabilize the stream flow and reduce bank erosion

Below is the project construction status update:

SC910 is approximately 98% complete with an expected construction completion of Summer 2021.

**Work in Progress / Complete**

- **Sewer construction**
  - All sewer construction work on this project was completed early February 2021.
- **Stream restoration work is underway from Walker Avenue towards Cedarcroft Road**
  - This is the final phase of stream construction work
  - Work entails of installing in-stream rock structures for flow control and bank stabilization features
  - Heavy machinery will be used (construction noise is expected)
  - Large construction vehicles will be utilized to deliver heavy stream building materials to the site
  - Stream flow will be rediverted and managed with bypass pumps (some operational noise is expected)
  - Work expected to take approximately 2-4 weeks to complete
- **Stream restoration planting work (Fall 2021)**
  - Tree, grass, and shrub planting is complete in areas where sewer/stream construction was finished.
  - This work aims to stabilize disturbed areas, reforest along the stream, and beautify the area.
  - Current locations where plantings are completed:
    - Chinquapin Run stream banks and paths between Herring Run Stream & Hillen Road, Hillen Road & Loch Raven Blvd, Loch Raven Blvd & Woodbourne Ave, Woodbourne Ave & The Alameda, The Alameda & Belvedere Ave, Belvedere Ave towards Northern Parkway, Northern Pkwy & E Lake Ave
  - Areas currently under construction (East Lake Ave to Walker Avenue along Chinquapin Run) will be planted and restored in Fall 2021, when seasonally appropriate.


- **Site restoration at various locations**

- Sidewalks, curbs, and alleys previously impacted by work will be restored
- Asphalt pavement roads and parking lots impacted by work will be restored
- Topsoil, seed, and grass will be installed
- Construction vehicles and machinery will be used

Below are some pictures to highlight work in-progress and recently accomplished:



Reach E Stream Restoration Work Complete,  
new grass and planting installations  
(between Belvedere & Northern Parkway)

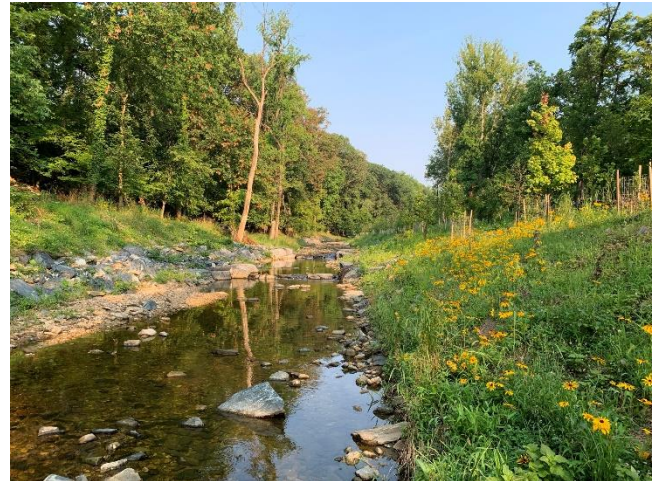

Reach B Stream Restoration Work  
Grasses and trees filling in  
(between Loch Raven & Hillen Road)

We hope this provides insights for upcoming work as we strive to timely and safely complete this project. If you have any questions, please call (410) 396-4700, Monday through Friday, between 8:30 AM and 4:30 PM. Additional information and resources are also available on our website <https://publicworks.baltimorecity.gov/>.

Sincerely,

Christopher Peake  
Construction Project Supervisor I  
DPW, Office of Engineering & Construction  
Christopher.Peake@baltimorecity.gov
