



Sanitary Contract 965 (Improvements to the Sanitary Sewers in the
North East area of Baltimore City)

December 1, 2020

To whom it may concern,
Below is the project construction status update

Work in Progress:

- Armistead Gardens Park Sewer Rehabilitation
Bypass pipe installation, pump station placement, Contractor prepares for lining.
- Sewer rehabilitation and manhole installation
Sanitary pipe replacement and rehabilitation behind 2919 Overland Avenue, , existing manholes rehabilitation.
Sewer repair at 3100 Harview, house laterals rehabilitation.

Upcoming Work (October 2020)

- Sanitary sewer replacement and rehabilitation in conjunction with manhole installation and rehabilitation will continue behind 2919 Overland Avenue.
Heavy machinery will be used (construction noise is expected).
Sewer flow will be rediverted and managed with bypass pumps (some operational noise is expected)
Work is expected to continue for approximately two months.
- Sewer rehabilitation will continue in Armistead Gardens Park.
Heavy machinery will be used (construction noise is expected).
Sewer flow will be rediverted and managed with bypass pumps (some operational noise is expected)
Work is expected to continue for approximately one more month.
- Sewer repair at 3100 Harview Ave., preparation for rehabilitation.
BGE has secured the existing pole at 3100 Harview Avenue, Point repair completed, sewer main lining performed, lateral lining will follow.
Heavy machinery will be used (construction noise is expected).
House connections seals will be installed using heavy equipment. Resin odors to be expected during curing process.

Below are some pictures to highlight work accomplished to-date.



2020/10/09 09:18
6523 Hilltop Ave
Baltimore



2020/10/09 15:05
6523 Walther Ave
Baltimore




2020/10/09 16:24
6519 Hilltop Ave
Baltimore



2020/10/09 16:58
6527 Hilltop Ave
Baltimore



2020/10/09 18:36
6523 Hilltop Ave
Baltimore

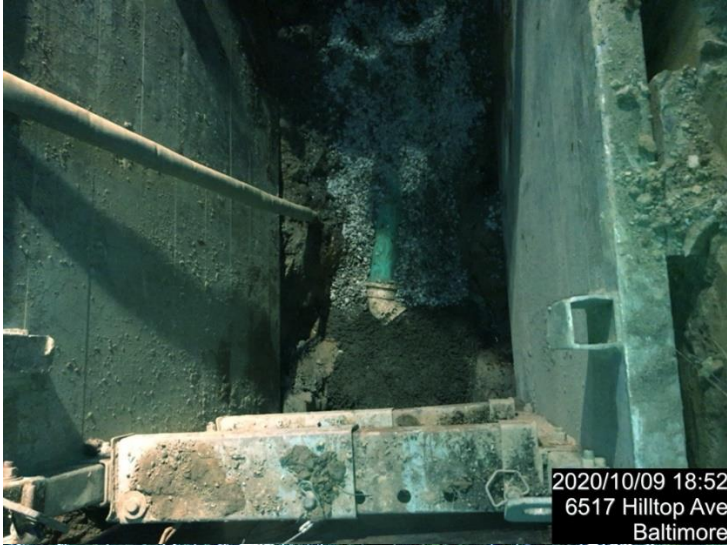

2020/10/09 18:52
6517 Hilltop Ave
Baltimore



2020/10/09 19:19
6522 Walther Ave
Baltimore



2020/10/24 15:4
6521 Hilltop Ave
Baltimore



2020/10/24 16:2
6523 Hilltop Ave
Baltimore



2020/10/24 17:0
6522 Walther Ave
Baltimore

We hope this provides insights for upcoming work as we strive to timely and safely complete this project. If you have any questions, please call (410) 396-4700, Monday through Friday, between 8:30 AM and 4:30 PM. Additional information and resources are also available on our website <https://publicworks.baltimorecity.gov/>.

Aurelian Nicolau

Aurelian Nicolau
Construction Project Supervisor I
DPW, Office of Engineering & Construction
Aurelian.Nicolau@baltimorecity.gov
