

CITY OF BALTIMORE

BRANDON M. SCOTT, Mayor



DEPARTMENT OF PUBLIC

Matthew W. Garbark, Acting Director
Abel Wolman Municipal Building, 6th
Floor 200 N. Holliday Street
Baltimore, Maryland 21202

Sanitary Contract 941 (Sewer Collection System Improvements in the Jones Falls Sewershed)

April 1, 2021

To whom it may concern,

Below is the construction status of project SC941.

Project Limits

The SC941 work area is within the Jones Falls Sewershed and includes work along the Jones Falls River and Falls Road. The Work Area is largely east of Interstate 83 and west of Route 1. This project will help eliminate two (2) of the City's Sanitary Sewer Overflows (SSO) - SSO 67 and SSO 72. Besides the ongoing impact at Falls Road, the other neighborhoods are impacted by Cured in Place (CIPP) lining, Manhole Rehabilitation, etc. These neighborhoods are in Districts 11, 12 and 14. Approximately completion of project to date is 67%.

Work in Progress

- Falls Road Closure
 - Closed as of 5/11/20
 - The Jones Falls Trail will still be open and accessible to the public
- Pre- CCTV for Cured In Placed Pipe (CIPP) Lining
 - Heavy machinery will be used (construction noise is expected)
 - Lane closures /lane adjustments are expected
- CIPP Lining, Sewer Rehabilitation
 - Heavy machinery will be used (construction noise is expected)
 - Lane closures /lane adjustments are expected
 - During curing process odor may be emitted
 - Completed Locations:
 - 03/01/2021: Ellsworth Ave 30" PCCP
 - 03/11/2021: 6116 Park Heights Ave.; Fords Lane at Fieldcrest Rd
 - 03/12/2021: 426 E Lorraine Ave
 - 03/15/2021: 212 E 23rd St
 - 03/17/2021: 212 E 23rd St
- Manhole Rehabilitation
 - Heavy machinery will be used (construction noise is expected)
 - Sewer flow will be rediverted and managed with bypass pumps (some operational noise is expected)

Please Visit our Website @ www.baltimorecity.gov

- Lane closures /lane adjustments is expected
- Completed/Ongoing Locations:
 - 03/01/2021: 2613 Barclay St
 - 03/03/2021: 6 W Lanval St; 2844 North Lovegrove Ave
 - 03/04/2021: Maryland Ave & Trenton Street; 2723 Greenmount Ave
 - 03/05/2021: 225 E Lafayette Ave; 421 East Lorraine Ave
 - 03/08/2021: 1617 N Calvert St; 2501 Barclay St
 - 03/11/2021: 1800 N Charles St.; 1300 N Charles St.; 2468 Brentwood Ave.
 - 03/12/2021: 301 E 27th St; 401 Barclay St; N Charles St and Lovegrove St.
 - 03/15/2021: 2467 Brentwood-Greenmount alley; 2323 Guilford-Falls; 3215 Bancroft Rd; 301 East 27th St; 6505 Williamson Ave
 - 03/16/2021: 3804 Bancroft Rd; 813 Cokesbury Ave; 28 W 27th St
 - 03/17/21: 3701 Bancroft Rd; 1817 North Ave-Lafayette Ave; 2453 Barclay St

Siphon - Tunnel and Confluence Structures, Grinder pumps at BSM and MICA, Pedestrian Trail Relocation

- Adjacent to 2101 Falls Rd
- Grinder Pump Installations at Baltimore Streetcar Museum (BSM) and Maryland Institute College of Art (MICA) are ongoing.
- Falls Rd Bypass demobilization is complete.
- Jones Falls Pedestrian Trail is no longer detoured, and the original route has been restored. Traffic barriers/guard rails installed.

Upcoming Work

- Falls Road Closure
 - Closed as of 5/11/20
 - Pedestrian Trail is open. All are requested to exercise with caution
- Pre- CCTV for Cured In Placed Pipe (CIPP) Lining
 - Heavy machinery will be used (construction noise is expected)
 - Lane closures /lane adjustments are expected
 - Upcoming Locations: TBD
- CIPP Lining, Sewer Rehabilitation
 - Heavy machinery will be used (construction noise is expected)
 - Lane closures /lane adjustments are expected
 - During curing process odor may be emitted
 - Upcoming Locations: TBD

Manhole Rehabilitation

- Heavy machinery will be used (construction noise is expected)
- Sewer flow will be diverted and managed with bypass pumps (some operational noise is expected)
- Lane closures /lane adjustments is expected
- Upcoming Locations: TBD

Siphon - Tunnel Shoring and Bypass Trail Relocation

- Activity Complete
- Trail route restored to original pattern.

Test Pit Excavation for Pressure Sewer Along Broadway

- Heavy machinery will be used (construction noise is expected)
- Lane closures /lane adjustments is expected

Pressure Sewer Installation Along Ellsworth St

- Heavy machinery will be used (construction noise is expected)
- Lane closures /lane adjustments is expected

Broadway Bypass Pumping

- Heavy machinery will be used (construction noise is expected)
- Lane closures /lane adjustments is expected
- Tree Removal along portion of bypass route
- Bypass piping anticipated to run at grade along N Broadway center median and below grade at Intersections from E. Oliver St to E. Chase St. Some detours are expected. There could be some impact to parking along Broadway (NB).



Below are some pictures to highlight work accomplished to-date.



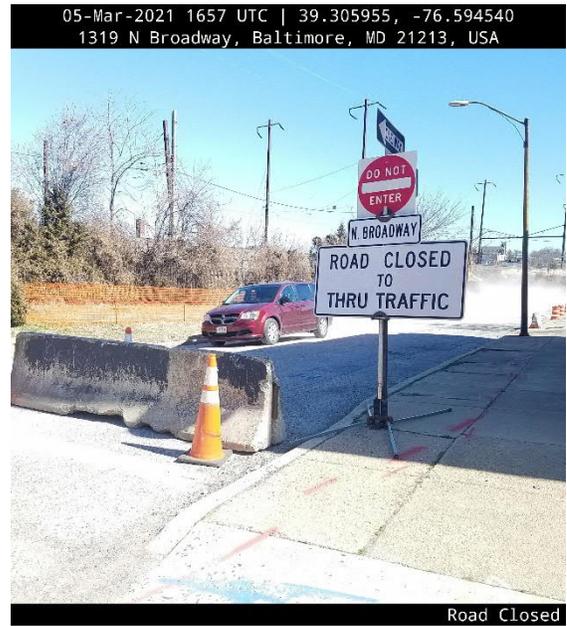
Manhole Rehab (Gist Ave)



Grinder Pump Installation (MICA)



Jones Falls Trail (Falls Rd)



Road Closure (Ellsworth St)

We hope this provides insights for upcoming work as we strive to timely and safely complete this project. If you have any question; you may call (410) 396-4700; Monday through Friday; between 8:30 AM and 4:30 PM. Also Mr. Indranil Goswami, the project manager can be reached at (410) 396-4700, as well as via email; Indranil.Goswami@baltimorecity.gov. Additional information and resources are also available on our website <https://publicworks.baltimorecity.gov/>.

Sincerely;

Indranil Goswami
Construction Project Supervisor I
DPW, Office of Engineering & Construction

@Printed on recycled paper with environmentally friendly soy based ink.
