




Sanitary Contract 946R
(Improvement to the Sanitary Sewers in the Jones Falls Sewershed – Glen Avenue)

3/22/2022

To whom it may concern,

The Sanitary Contract 946R has a project scope that includes the closing of a 12-inch sanitary sewer overflow (SSO) pipe draining to the City’s storm drain system identified as SSO155, upsizing/increasing the flow capacity of 3,000 LF of 8-inch sewer main along Glen Avenue and the structural rehabilitation of 82 manholes, 392 LF of 12-inch main, 375 LF of 10-inch main, 10,564 LF of 8-inch sewer main and 236 LF of 6-inch sewer main. The project is currently in the design phase.

Project Limits:

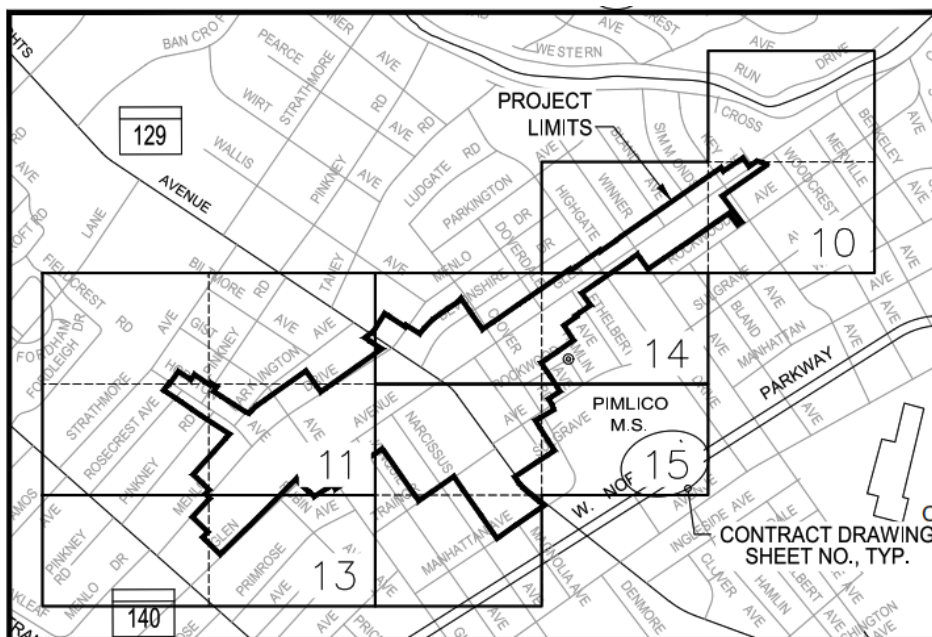

Below is the current project design status update:

The project is at 100% design phase while addressing the comments from the different agencies.

Constructability review comments have been addressed.

Most updated boiler plate of the Office of Engineering and Construction Specifications has been revised with the most recent guidelines and specifications.

Permits are being applied for prior to the start of the construction phase of the project.

State MBE and WBE goals are being outlined in the contract specifications.

Second round for Right of Entry form agreements will be sent out to home owners before Article 25 is issued to non-responding home owners.

@Printed on recycled paper with environmentally friendly soy based ink.
