

# DEPARTMENT OF PUBLIC WORKS

## Sanitary Sewer Modified Consent Decree

### Project Facts



## SC #1020R:


### CCTV Inspection of Sanitary Sewers in Northern Baltimore City

#### Project Purpose

To comply with the conditions of the City's Modified Consent Decree with the U.S. EPA and MDE

- To inspect a sewer system that is up to 100 years old
- To prioritize pipe rehabilitation work through condition assessment
- To indirectly:
  - improve sewage flows and pipe capacity
  - To reduce/eliminate sewer overflows
  - To eliminate street closures due to sewer pipe collapses
  - To improve water quality in streams
  - To prevent sewer back-ups into private property


#### Project Area Map

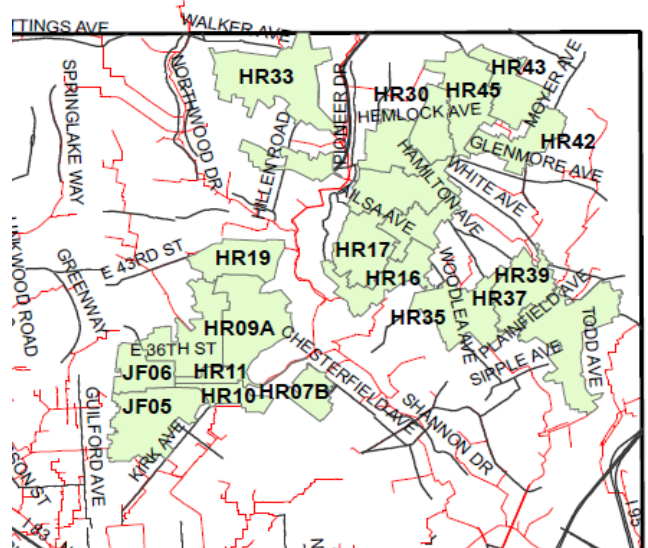

#### Project History

In 2002 the City of Baltimore (City) entered a Consent Decree with the U.S. Environmental Protection Agency (EPA) and the Maryland Department of the Environment (MDE). A Consent Decree is an agreement made in court by the parties to settle a suit in equity. In 2017, the Modified Consent Decree (MCD) was entered to address sewer system deficiencies in a proactive program by 2030. More information on the Consent Decree can be found at: <http://publicworks.baltimorecity.gov/>

#### Project Schedule

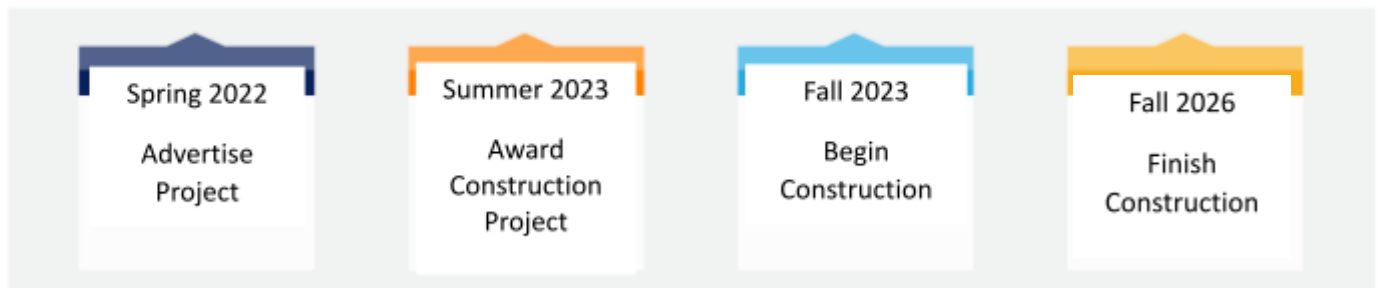

# DEPARTMENT OF PUBLIC WORKS

## Sanitary Sewer Modified Consent Decree

### Project Facts



## SC #1020R:

### CCTV Inspection of Sanitary Sewers in Northern Baltimore City

#### Project Updates

- NTP given to Contractor in October 2023.
- Contractor currently working on Work Order #1, #2, #3 and #4 and completed 180,000 LF and over 650 MHs as of 12/13/2024.



#### Project Activities

- Approx. 551,000 linear feet (LF) of CCTV inspection of 6” through 8” diameter sanitary sewers
- Approx. 104,000 linear feet (LF) of CCTV inspection of 10” through 12” diameter sanitary sewers
- Approx. 33,000 linear feet (LF) of CCTV inspection of 14” through 18” diameter sanitary sewers
- Approx. 13,000 linear feet (LF) of CCTV inspection of 20” through 24” diameter sanitary sewers
- Approx. 13,000 linear feet (LF) of CCTV inspection of 25” through 29” diameter sanitary sewers
- Approx. 2,000 linear feet (LF) of CCTV inspection of 30” through 34” diameter sanitary sewers
- Approx. 13,000 linear feet (LF) of CCTV inspection of 36” through 57” diameter sanitary sewers
- Approx. 9,000 linear feet (LF) of CCTV inspection of 60” through 90” diameter sanitary sewers
- Approx. 30,000 linear feet (LF) of SONAR inspection of 20” through 90” diameter sanitary sewers
- Approx. 10,000 linear feet (LF) of LASER inspection of 36” through 90” diameter sanitary sewers – data collection
- Approx. 10,000 linear feet (LF) of LASER inspection of 36” through 90” diameter sanitary sewers – post processing
- Approx. 551,000 linear feet (LF) of cleaning of 6” through 8” diameter sanitary sewers
- Approx. 104,000 linear feet (LF) of cleaning of 10” through 12” diameter sanitary sewers
- Approx. 33,000 linear feet (LF) of cleaning of 14” through 18” diameter sanitary sewers
- Approx. 13,000 linear feet (LF) of cleaning of 20” through 24” diameter sanitary sewers
- Approx. 13,000 linear feet (LF) of cleaning of 25” through 29” diameter sanitary sewers
- Approx. 2,000 linear feet (LF) of cleaning of 30” through 34” diameter sanitary sewers
- Approx. 5,400 each (EA) Manhole Inspections

If you have any project-related questions, please call (443) 986 - 1630, Monday through Friday, between 8:30 AM and 4:30 PM. Additional information and resources are also available on our website <https://publicworks.baltimorecity.gov/>



Project # 1410 / [Sample of Community Outreach Update page](#)
